


North Wokingham Distributor Road - West Of Old Forest Road (Incorporating Winnersh Relief Road Phase 2) -

Newsletter - November 2020

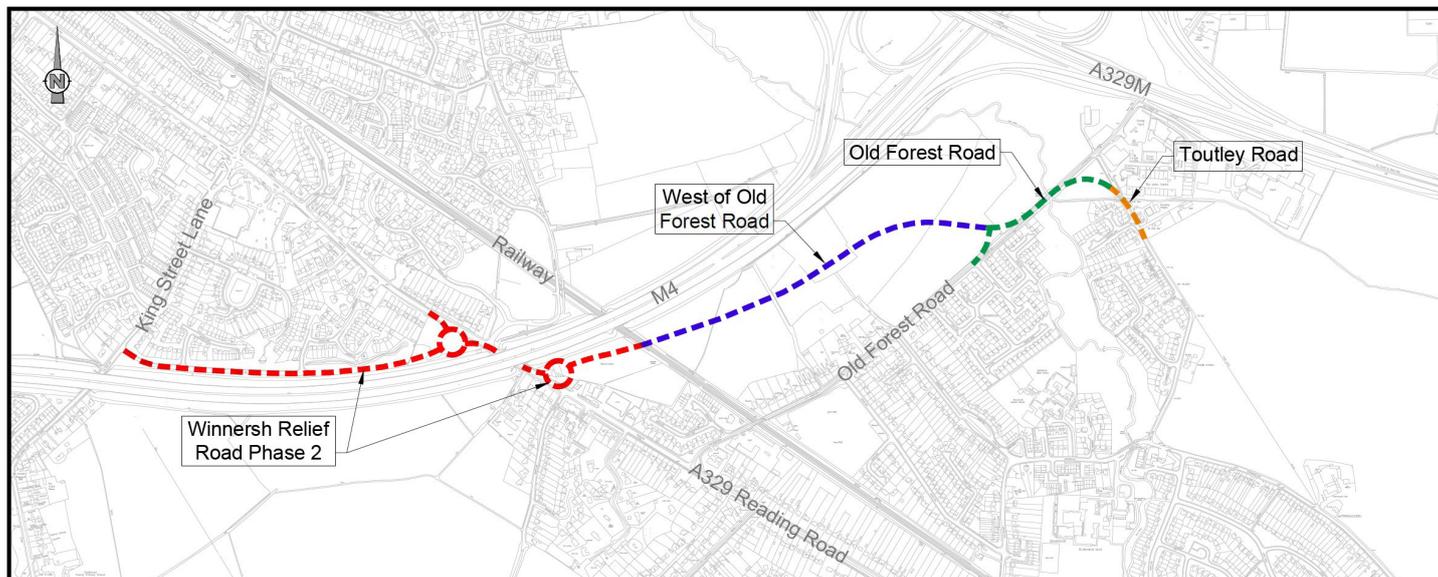

» Work to date

Works are continuing to progress across all sections of the project. As we fast approach the winter months with the changing weather, along with shorter days and longer nights, we are continuing to review and assess our works in line with Government advice and guidance, placing the safety of our workforce and the public as top priority.

Works are progressing and, as is stands, we are still on track to complete the scheme early 2022.

North Wokingham Distributor Road – West Of Old Forest Road (Incorporating Winnersh Relief Road Phase 2) -

Newsletter – November 2020

» Winnersh Relief Road



Vacuum excavation works being carried out in line with social distancing guidelines



New temporary site access by the BP garage on Reading Road where existing underground utilities are being lowered



Foundation of the new northern roundabout (north of the M4) under construction



Foundation of the new northern roundabout (north of the M4) under construction

» Old Forest Road



Ground preparation for caissons which will be used for the foundation of the new footbridges in the Emmbrook watercourse



Delivery of concrete rings to be assembled



Concrete pour in assembled caisson

North Wokingham Distributor Road - West Of Old Forest Road (Incorporating Winnersh Relief Road Phase 2) -

Newsletter - November 2020

A caisson foundation is most often used in the construction of bridge piers and other structures that require foundations beneath rivers and other waterbodies. It is a prefabricated hollow box or cylinder sunk into the ground to the desired depth and then filled with concrete thus forming a foundation.



Flood alleviation scheme in progress at the corner of Old Forest Road and Toutley Road

» West of Old Forest Road



Finished embankment leading to the new railway bridge. The embankment is 8m higher than the original ground. The finished level of the embankment is expected to be at the same level as the M4 as this is the height required to clear the railway



Sheet piling being installed



Sheet piling installation completed. The system will protect the railway during the new bridge piling work

North Wokingham Distributor Road - West Of Old Forest Road (Incorporating Winnersh Relief Road Phase 2) - Newsletter - November 2020




The piling rigs are assembled and reinforcement steel prepared



Rotary excavation for the piles is progressing. Piling work is taking place on both sides of the railway simultaneously. The tall blue cranes can be seen from the Reading Road and surrounding area

» Culvert installation

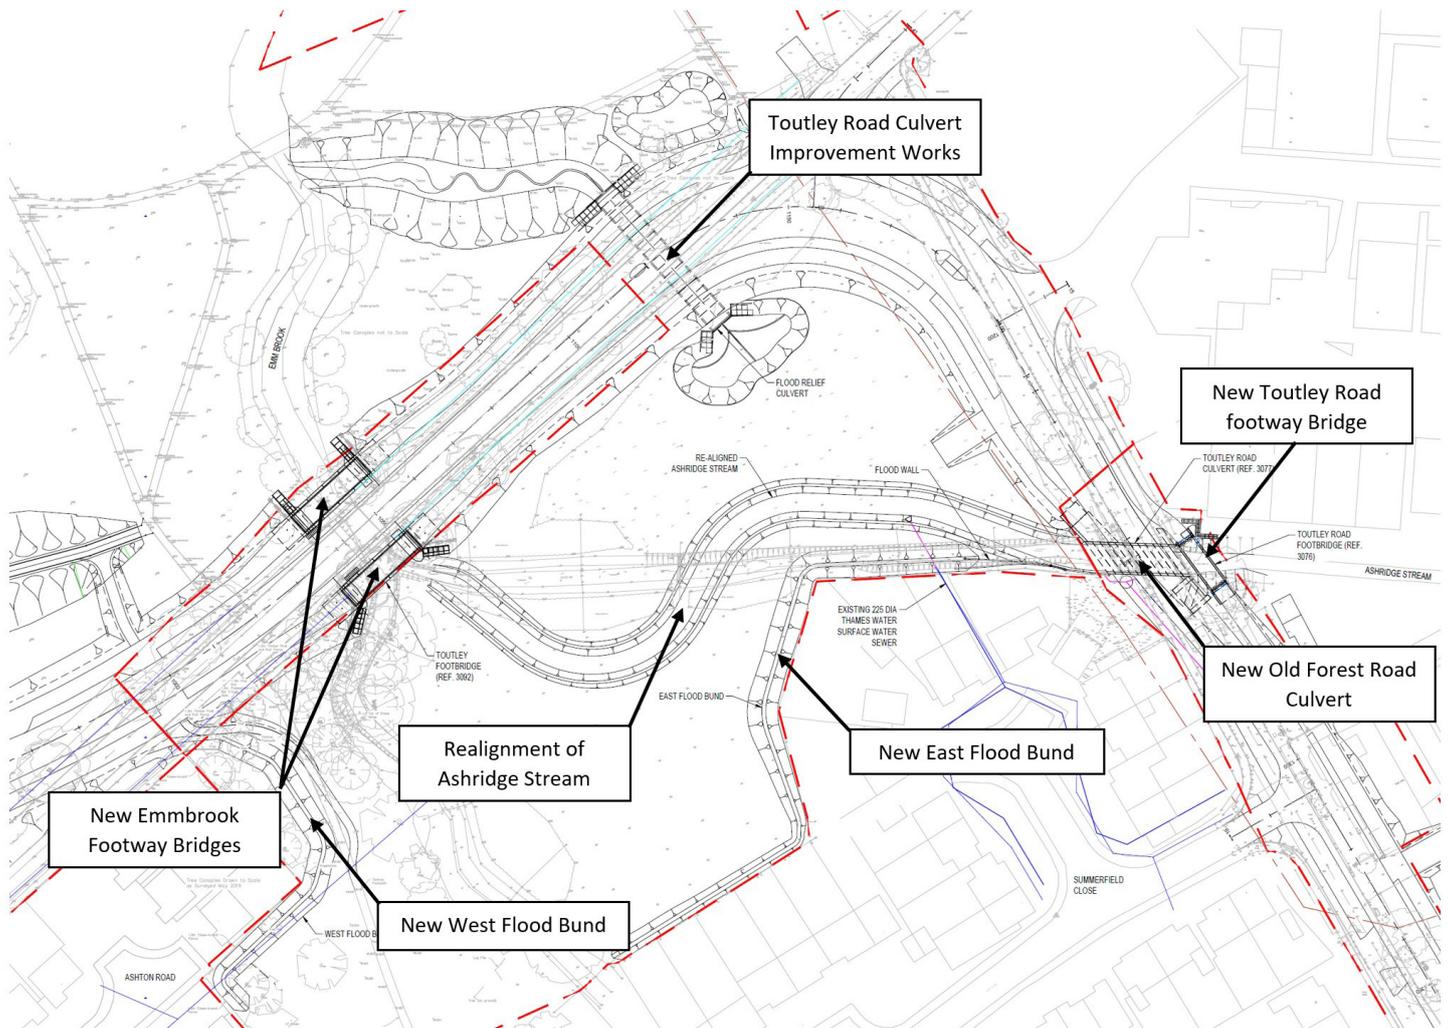

North Wokingham Distributor Road – West Of Old Forest Road (Incorporating Winnersh Relief Road Phase 2) -

Newsletter – November 2020



From left to right, clockwise: delivery; crane lifting



Joint installation



Finished section of flood culvert

» Upcoming works

These tables show planned works, split by section of road, between now and end of this project. of Please note these are indicative dates and are subject to change at short notice due to reasons beyond our control

» Did you know?

The total amount of new utility ducting we are installing as part of this project is 11.5km as well as 3.8km of new drainage pipes

Winnersh Relief Road Phase 2 (Longdon Road to Reading Road)

Brief description of works	Estimated Timeline
Kerbs	November 2020
Surfacing	November - December 2020
Expected completion	End of December 2020

North Wokingham Distributor Road – West Of Old Forest Road (Incorporating Winnersh Relief Road Phase 2) -

Newsletter – November 2020

Old Forest Road	
Brief description of works	Estimated Timeline
Installation of new footbridges across the Emmbrook, installation of new flood relief culvert	September - October 2020
Earthworks and site clearance to allow way for main construction	September 2020 - January 2021
Laying of kerbs	January 2021
Installation of drainage	December 2020 - March 2021
Road surfacing	February - March 2021
Switch over to Toutley Road	End of March 2021

West of Old Forest Road	
Brief description of works	Estimated Timeline
Piling work	October - December 2020
Installation of abutments - see description underneath	December 2020
Bridge preparation	November 2020 - January 2021
Crane lifting and installation of steel beams	January - February 2021
Installation of wing walls - see description underneath	January - March 2021
Installation of bridge deck by phased concrete pours	March - May 2021
Expected completion	June 2021

Toutley Road	
Brief description of works	Estimated Timeline
Main construction	March 2021 - March 2022
Expected completion of overall scheme	March 2022

» Upcoming traffic management & road closures

Period	Peak/off-peak	Location	Section of road	Description of works
October - December 2020	Off-peak	Reading Road junction with Woodward Close	Temporary traffic lights	
Please note: Overnight works over three nights (8pm - 6am) are planned commencing 9th November on the Reading Road by the BP station and Woodward Close to accommodate a change of traffic management layout.				
September 2020 - March 2021	Full road closure	Old Forest Road	Full road closure	
April 2021 - November 2021	Full road closure	Toutley Road	Full road closure	

Daily public safety will remain a priority, as will access to the Emergency Services. Additionally, access for local residents will remain open at all times.

North Wokingham Distributor Road – West Of Old Forest Road (Incorporating Winnersh Relief Road Phase 2) -

Newsletter – November 2020

As we draw closer to the winter months, our construction site will be lit to allow us to continue working during darker hours. Lights will be turned off during the night. We apologise in advance for any inconvenience and kindly ask you to bear with us whilst these essential works are carried out.

Council relaunches traffic and travel social media to keep residents up to speed

Wokingham Borough Council's 'Traffic and Travel' social media accounts, dedicated to keeping residents up to speed with the roadworks around the borough that may affect their journey times, have been relaunched this month. You can follow the council's traffic and travel 'social pages by visiting www.facebook.com/WokinghamRoadWorks and www.twitter.com/TrafficAlert



Also, for more information on roadworks you can visit [one.network](#), an online platform which provides the latest information about upcoming works.

CONTACT US

If you know of anyone in your local community who does not have access to the internet but would like to receive this e-newsletter, please let us know. Wokingham Borough Council, in partnership with Balfour Beatty have a dedicated project team should you have any questions or concerns. E-mail us at NWDR@balfourbeatty.com or telephone **0800 121 4444**.

For further information please visit: www.wokingham.gov.uk/roadworks-and-outdoor-maintenance/major-new-roads/
